

Report Date 5/10/2007

Company G-MAN INSPECTION SERVICES, LLC
Address 4811 Corkwood Lane Orlando, FL 32808
Thermographer Carlos Guzman

Customer Sample
Site Address 123 MainUSA
Contact Person John Doe

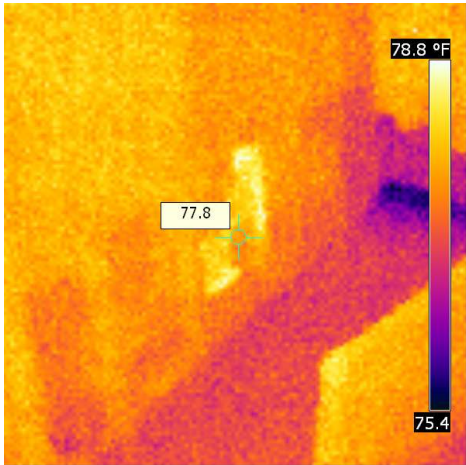


Image and Object Parameters		Text Comments
Camera Model	FLIR B-CAM Western S	
Image Date	2007:05:10 09:02:20	
Image Name	IR_0059.jpg	
Emissivity	0.95	
Reflected Temperature	84.0 °F	
Object Distance	6.6 ft	

Description

IR image: back of tile shower area (drywall removed for clarity). Shower was active with hot water (10 min. test). It appears that the grout/aggregate and liner has failed, allowing the heat to reflect on surface thus potential cause for leaks.

Report Date 5/10/2007

Company G-MAN INSPECTION SERVICES, LLC
Address 4811 Corkwood Lane Orlando, FL 32808
Thermographer Carlos Guzman

Customer Sample
Site Address 123 MainUSA
Contact Person John Doe

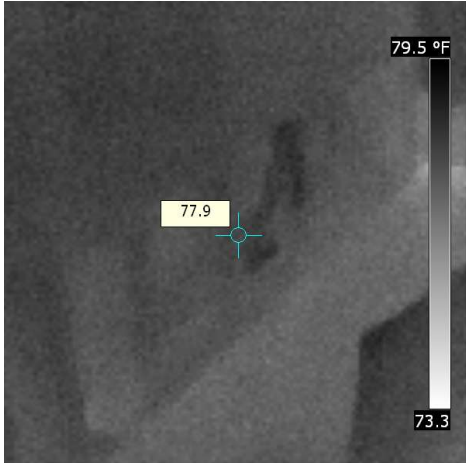


Image and Object Parameters		Text Comments
Camera Model	FLIR B-CAM Western S	
Image Date	2007:05:10 09:22:57	
Image Name	IR_0057.jpg	
Emissivity	0.95	
Reflected Temperature	84.0 °F	
Object Distance	6.6 ft	

Description
How shower test. Moisture meter used to validate moisture findings. Replacement of shower enclosure recommended

Report Date 5/10/2007

Company G-MAN INSPECTION SERVICES, LLC
Address 4811 Corkwood Lane Orlando, FL 32808
Thermographer Carlos Guzman

Customer Sample
Site Address 123 MainUSA
Contact Person John Doe

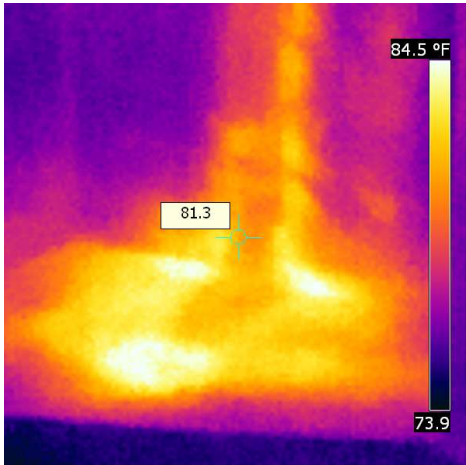


Image and Object Parameters		Text Comments
Camera Model	FLIR B-CAM Western S	
Image Date	2007:05:10 09:20:28	
Image Name	IR_0061.jpg	
Emissivity	0.95	
Reflected Temperature	84.0 °F	
Object Distance	6.6 ft	

Description
stand up , tile shower. Hot water test (10 min)
